

PAINT AND COTTAGE CONCEPT · WILLIAMSBURG, MICHIGAN

10746 E Deal Road

Whitewater Township · Grand Traverse County · Elk Lake views

> A paint and cottage concept for 10746 E Deal Road. On the main and upper levels, walls are Sherwin-Williams Shoji White, and trim, doors, railings, and wall paneling are Alabaster — except the main living room, which stays in its original darker colors for a piano night-club lounge feel. The lower walkout uses a warmer beige, Accessible Beige, on the drywall only; the existing wood paneling, doors, trim, and railings downstairs stay natural. Kitchen and bath cabinets are Benjamin Moore Edgecomb Gray. Natural wood ceilings and beams stay as they are throughout. Outside is a country-modern scheme: Alabaster siding, Tricorn Black trim, and Iron Ore railings, with the existing 2019 roof kept. A 2 bedroom, 2 bath modular cottage of about 1,040 square feet is shown on the 4.67-acre east land (parcel 13-002-018-30), northeast of the house and the front barn — not on the 0.46-acre strip directly north of the house. It sits off the electric-line corridor, with its long axis running north–south so the porch faces the lake, a two-car parking pad on the west side, its own driveway, a walking trail to the main house, and the front barn and existing trees helping to screen it from parts of the house. Every painted photo below opens on the new colors. Drag any of those photos to see the original listing shot. These are visualizations, not a contractor proposal.

The house

BEDS / BATHS	FINISHED AREA
6 / 3.1	3,120 sf

LOT	YEAR BUILT
9.35 acres	1993

ADDRESS	TOWNSHIP	STYLE	ABOVE / BELOW GRADE	LOT
10746 E Deal Rd, Williamsburg, MI 49690	Whitewater Township, Grand Traverse County	2-story contemporary with a finished walkout	1,956 sf above + 1,164 sf finished lower level	9.35 acres, rolling and wooded, with Elk Lake views

GARAGE	OUTBUILDINGS	EXTERIOR	HEAT / COOLING	WATER / SEWER
Attached, about 2.5 cars	Two pole barns, 30×40 and 35×40, plus a smaller yard shed	Vinyl siding, asphalt roof (replaced in 2019 on the house and one barn)	Natural gas hydronic / baseboard, wood fireplace, ductless A/C	Private well and septic

SCHOOLS	LEVELS IN THIS CONCEPT
Elk Rapids Schools	Main and upper in Shoji White, except the living room, which is kept as-is; lower walkout in Accessible Beige with natural wood paneling

Open the main property concept page

Interior color palette

The main and upper levels use a light Shoji White wall color, except the main living room, which is left in its original darker colors. The lower walkout uses a warmer beige on the painted drywall only, and keeps more of the wood paneling natural. Wood ceilings and structural beams stay natural everywhere. Floors, counters, appliances, fixtures, furniture, windows, and fireplace stone stay as they are.

Shoji White

Sherwin-Williams SW 7042

Walls on the main and upper levels, including bedrooms, baths, halls, and the loft walk — but not the main living room.

Approx. hex #E6DFD3 · Eggshell or matte on walls

Accessible Beige

Sherwin-Williams SW 7036

Painted drywall on the lower walkout only. A warmer, more beige tone than the rooms upstairs.

Approx. hex #D1C7B8 · Eggshell or matte on walls

Alabaster

Sherwin-Williams SW 7008

Trim, doors, railings, and wall paneling on the main and upper levels. Not used on the lower-level wood, and not on ceiling boards or structural beams.

Approx. hex #EDEAE0 · Semi-gloss on trim and doors

Edgecomb Gray

Benjamin Moore HC-173

Main kitchen cabinets and island, laundry cabinets, bathroom vanities and linen cabinets, and the lower-level kitchen cabinet. Countertops stay as they are.

Approx. hex #D9D3C4 · Satin urethane enamel

What stays untouched inside

The main living room keeps its original darker colors. On the lower walkout, existing wood wall paneling, doors, trim, and railings stay the natural honey wood. All wood tongue-and-groove ceilings and structural beams remain natural throughout the house. Already-white drywall, popcorn, and drop ceilings stay white. Hardwood, carpet, and tile floors, granite counters, tile backsplashes, appliances, fixtures, furniture, window glass and views, and the stone fireplace are unchanged.

Interior concept

Each photo shows the new colors. Drag any photo to the right to see the original listing photo.

Main kitchen



Main kitchen



Kitchen sink and backsplash

Dining area

The sloped wood wall paneling is painted Alabaster. The honey wood ceiling boards stay natural.



Dining area

Main living room

Kept as-is. The existing darker colors stay, for a piano night-club lounge feel. These rooms are not part of the paint concept and are not included in the interior painting cost.



Living room, looking toward the view



Living room and fireplace



Fireplace close-up

Primary bedroom

The salmon walls go to Shoji White. The wood wall paneling and door are Alabaster. The wood ceiling, skylight, and beam stay natural.



Primary bedroom

Primary bath



Primary bath vanity



Primary bath shower

Main-floor laundry



Laundry

Upper level

The wood-paneled loft walk, doors, trim, and railing are Alabaster. The bedroom at the end of the hall is Shoji White. The living-room vault visible from the loft keeps its original darker color, so the lounge below stays as-is.



Upper hall and loft railing



Upper bedroom



Upper bedroom with paneled closet

Main-floor powder room



Powder room

Lower walkout

A different, more beige wall color downstairs: Accessible Beige on the painted drywall only. The existing wood wall paneling, stair, doors, trim, and railings stay natural honey wood. The lower kitchen cabinet is still Edgecomb Gray.



Lower family room and stair



Lower hallway



Lower bedroom



Bedroom with paneled wall



Lower kitchen

The unfinished mechanical room in the listing photos is left as-is and is not part of the paint scope.

Exterior concept

A country-modern look: a light Alabaster body, black window and door trim, and dark charcoal railings, with the existing 2019 asphalt roof kept. The house siding is vinyl, so light body colors such as Alabaster are the safe choice. No roof replacement is part of this concept.

Alabaster

Sherwin-Williams SW 7008

Vinyl siding on the house, garage wing, and shed. Soft creamy off-white.

Approx. hex #EDEAE0

Tricorn Black

Sherwin-Williams SW 6258

Fascia, soffit, window and door trim, gutters, downspouts, and the walkout door.

Approx. hex #2F2F2F · Semi-gloss on trim

Iron Ore

Sherwin-Williams SW 7069

Deck railings, stair railings, and deck posts. Deck floor boards stay the existing wood.

Approx. hex #434341

Vinyl-safe paint

The siding is vinyl. Light colors such as Alabaster are generally safe to use on vinyl. Darker body colors can warp or buckle vinyl unless they are mixed in a vinyl-safe formula, such as Sherwin-Williams VinylSafe. Regular Iron Ore (SW 7069) and Tricorn Black (SW 6258) are not VinylSafe body colors; do not use them on the siding itself. They are fine on wood or metal trim, doors, gutters, and railings.

Main elevation

Alabaster siding and black trim, with the existing 2019 shingle roof left as it is.

Each photo shows the new colors. Drag any photo to the right to see the original listing photo.



Paint only, existing roof kept

Other exterior views

The same paint scheme, with the existing roof kept wherever it is in the frame. Drag to see the original.




Rear elevation and yard shed, existing roof kept



Patio side, existing roof kept



Lower walkout under the deck

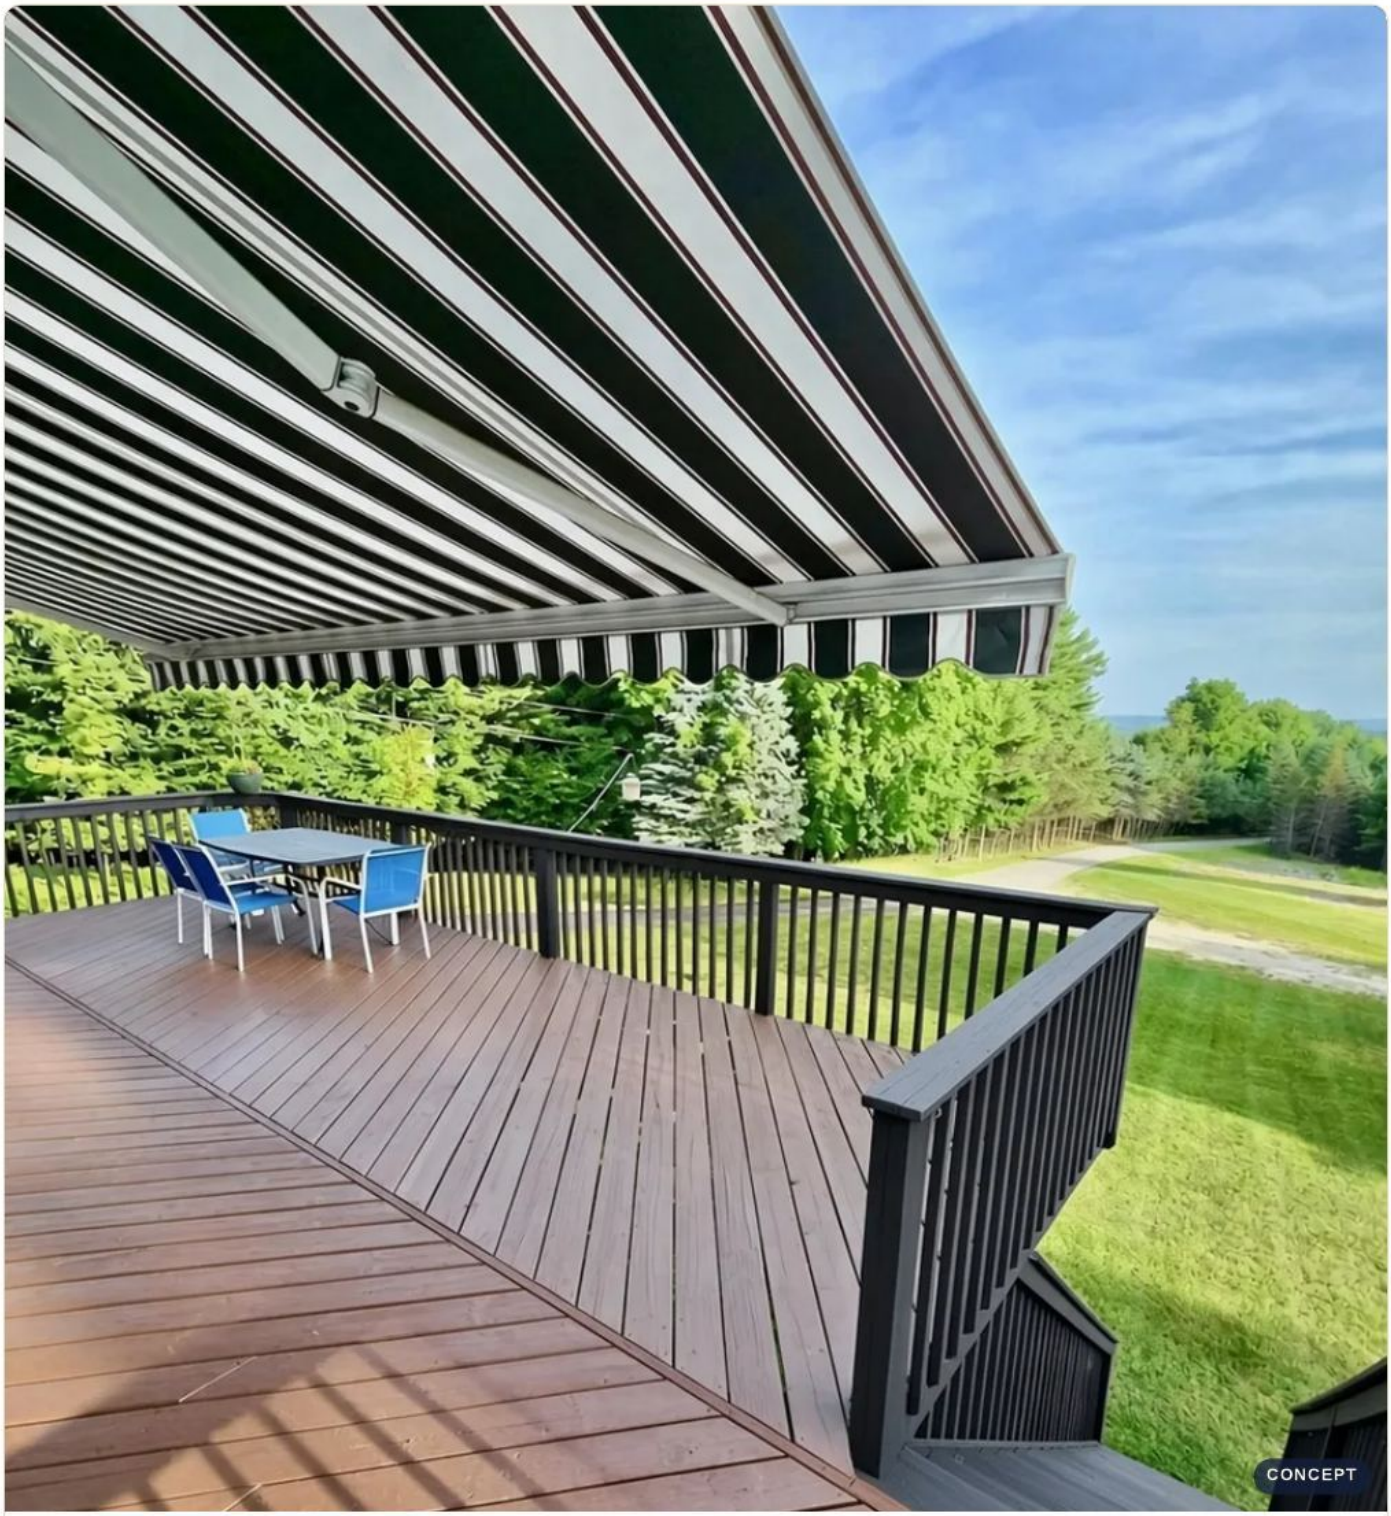

Deck railings in Iron Ore

Elk Lake views

These listing views are unchanged. They are included for setting only.



Elk Lake view



Lake view, fall color



Summer lake view



Evening light over the lake

Outbuildings

The two pole barns — one 30×40 and one 35×40 — are shown in the same country-modern scheme as the house: an Alabaster-light body, Tricorn Black trim and doors, and a dark metal roof. The smaller shed in the rear-yard photo above is painted to match.

> **Each photo shows the new colors.** Drag any photo to the right to see the original listing photo.



Pole barn, light body and black trim



Second pole barn, light body and black doors

Cottage on the east land

A **2 bedroom, 2 bath** Michigan modular cottage of about 1,040 square feet is shown on the east land, one of the three existing parcels. It has a kitchen, a living room, a utility / laundry room, and a two-car parking pad outside.

> **It is not on the small parcel directly north of the house.** That strip is parcel 13-002-018-01, 0.46 acre, immediately north of the house parcel and only about 100 by 200 feet. The cottage is on the larger east land, parcel 13-002-018-30, 4.67 acres, which runs as a long north–south lot along the east side of the house. Both the recommended pad (F) and the farther-north alternate (N) are on that east land. Pad F is about 300 feet northeast of the house and about 220 feet northeast of the front barn. Pad N is farther north on the same parcel, in denser pines; it is not on the 0.46-acre strip either.

The recommended placement, pad F, is **northeast of the house and the front (north) barn**, toward Elk Lake and well off the electric-line corridor that crosses the south field. An earlier concept sat just southeast of the south (rear) barn; that open field is the cleared power-line corridor, so that pad is not used. Placement was re-checked against a fresh Grand Traverse County leaf-off ortho, the county parcel lines, and the listing photos. Buildings and the driveway were re-digitized from that ortho: the earlier site-plan point for the front barn was about 39 feet too far northeast, which made the cottage look closer to that barn than it is. The cottage's long axis runs **north–south** so the catalog porch on the living-room end faces north / north-northwest toward Elk Lake. Bedrooms face south, toward the front barn. The front door and the two-car parking pad face west, toward a new gravel driveway spur of about 190 feet (about a 5% grade) and the front barn. A walking trail, kept off the driveway, runs from the east deck through the trees to the cottage. The front barn and existing trees help screen the cottage from parts of the main house; bare-earth line-of-sight from the decks is still open, so keep and add plantings. These drawings are concepts, not a survey, and permits would be required. A full topo and siting review of all three parcels is on this site.

These are concepts. Placement is approximate. The site plan is not a survey, and the rendered views are visualizations of a recommended Michigan modular cottage in the same country-modern palette as the house concept: Alabaster body and Tricorn Black trim. In the relationship views, the existing house and barns are shown as they look in the listing photos, not in the painted scheme.

Existing conditions, with parcel lines



Existing conditions from the Grand Traverse County leaf-off ortho, with county parcel lines. The 0.46-acre strip directly north of the house is 13-002-018-01. Pad F and pad N both sit on the 4.67-acre east land, 13-002-018-30, northeast of the house. Approximate, not a survey.

Site plan in relation to the main house




CONCEPT · annotated aerial of the three parcels. The cottage sits on the 4.67-acre east land (13-002-018-30), northeast of the house and the front barn — not on the 0.46-acre strip north of the house. The long axis runs north–south, with the porch on the north end facing the lake and a two-car parking pad on the west side. Buildings were re-digitized from the county ortho. Approximate, not a survey.

Recommended modular: Rochester American R31-26

The right product for this site is a **Michigan state-code modular** of about 900–1,200 square feet, 2 bedrooms and 2 baths, set on a permanent foundation. Modular homes are built to the same codes as a site-built house. Two local dealers that serve Grand Traverse County are Pine Grove Homes in Traverse City (231-947-6561) and Little Valley Homes in Cadillac (231-775-8102). Pine Grove already sells Rochester 26-foot ranch modulars.

The plan used for the footprint and concept views is the Rochester Homes American R31-26: 26′2″ × 40′0″, 1,040 square feet, 2 bed / 2 bath, with a kitchen, living room, and a utility / laundry room. An optional 8-foot covered porch sits on the living-room short end — that is why the cottage is turned north–south, so the porch faces the lake. The front door is on a long wall; here that door and the parking pad face west. Confirm a current package price with the dealer; a home-only package in this size typically runs about $120,000–$200,000 depending on finishes. A slightly larger alternate is the Jefferson R34-26 (26′2″ × 44′, 1,144 sf, 2 bed / 2 bath). Little Valley's Cozy Cabin, a Ritz-Craft modular, is 2 bed / 2 bath and 1,297 square feet, a bit over this size band. Other dealer pages for the R31-26 include Modular Homes of Michigan and Thorne's Homes.

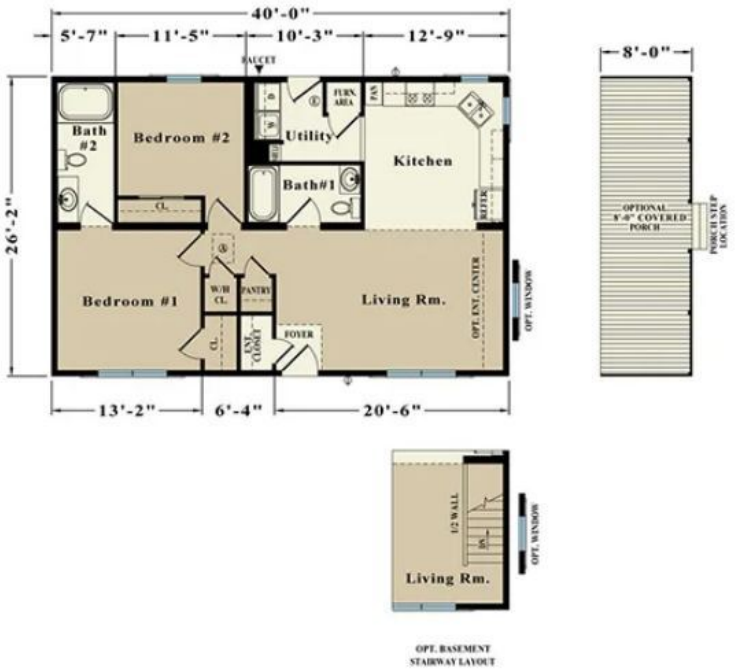

American R31-26 floor plan, from Rochester Homes. 26′2″ × 40′0″, 1,040 sf, 2 bed / 2 bath, utility / laundry, kitchen, and living room. The optional 8-foot porch is on the living-room end, which faces the lake in this concept.

Amazon does sell prefab structures, including a two-level foldable house listed at $42,000 (ASIN B0HPLG8CF7). That listing's own floor area is about 409 square feet, and it does not state HUD or Michigan modular approval. Shipping copy on the listing describes export to Latin America. It is unlikely to be permitted as a dwelling in Whitewater Township and is not recommended here. Other Amazon "1,200–5,000 sf villa" prices could not be verified, and at least one steel "modular house" at about $20,000 is a framing kit, not a finished home.

A HUD-code manufactured home can be cheaper, but many models in this size band use a different code, which can affect financing and resale. Use that path only if the township and a lender are comfortable with it.

Concept views from the house, barns, and cottage

The south-looking aerial below is the real Grand Traverse County leaf-off ortho, with only the cottage, a gravel spur, and a faint trail edited in. The other five views are photoreal concepts, checked against that ortho and the site plan. The house and both barns keep their real listing materials — grey-blue siding, the existing roof, and the metal barns as they stand today. Only the cottage is shown in the Alabaster and black country-modern finish. Positions and distances come from the labeled satellite and site plan: about 300 feet from the house and about 220 feet from the front barn, on the 4.67-acre east land (13-002-018-30), not on the small strip north of the house. A few views still show more open ground than the real woods, and some distances may read a little closer than they would on site.



CONCEPT · cottage, parking pad, and driveway spur placed on the real county ortho. The house and both barns are the actual buildings in their true positions. Approximate, not a survey.



CONCEPT · from the south, looking north, on the real county ortho: the house, both barns, and the cottage to the northeast. The front (vehicle) barn is east of the house; the south (gym) barn is in the foreground.



CONCEPT · from the east deck, looking northeast. The front barn is close on the left; the cottage sits farther back in the trees, about 300 feet from the house.



CONCEPT · from the cottage porch, looking toward Elk Lake. The real view will depend on trees and should be confirmed on the ground, preferably leaf-off.



CONCEPT · from the cottage, looking southwest. The front barn is in the mid-ground, seen from the northeast; the house sits uphill just beyond it.



CONCEPT · arriving on the cottage driveway and two-car parking pad, on the west side. The front door is on the west wall; the porch is on the north end, at left.



CONCEPT · from the front barn, looking northeast toward the cottage. The porch is on the north end; parking is on the west side, toward the barn and drive.

Planning cost, including site work

Planning ranges for a 2 bed / 2 bath, 1,040 sf Michigan modular on the east land in 2026, with a crawl-space foundation, a new well and a septic sized for two bedrooms, electric and plumbing, a short gravel driveway and two-car parking pad, modest porch, and professional setting. These are not bids. A perc test, a dealer quote, and township confirmation will tighten the numbers. The east parcel does not have its own Deal Road frontage, so the cottage driveway is planned as a spur off the existing drive; confirm that access and utilities are allowed before spending on a foundation.

SCOPE	LOW	TYPICAL	HIGH
Home package (factory, delivery, and set)	$120,000	$155,000	$200,000
Foundation (crawl space)	$14,000	$22,000	$32,000
New septic sized for 2 bedrooms (conventional at the low and typical end; mound at the high end)	$7,000	$12,000	$28,000
Private well, pump, and tank	$8,000	$12,000	$18,000
Electric service and run	$7,000	$13,000	$22,000
Plumbing hookups	$4,000	$7,000	$10,000

SCOPE	LOW	TYPICAL	HIGH
Cottage driveway, about 190 ft of gravel, plus a two-car parking pad	$8,000	$14,000	$22,000
Clearing, grading, and pad	$6,000	$12,000	$22,000
Township and county permits	$3,000	$5,000	$8,000
Porch or deck, skirting, and finish connections	$8,000	$16,000	$28,000
Contingency, about 12%	$22,000	$32,000	$47,000
Typical total, recommended 2 bed / 2 bath modular	**$207,000**	**$300,000**	**$437,000**

A perc test will decide whether a conventional septic is possible or whether a mound system is required. The typical column, about $300,000, is the planning number for a quality 1,040 sf modular with ordinary site conditions. Confirm zoning, access, well, and septic with Whitewater Township and Grand Traverse County Environmental Health before bidding the work. Home-package prices should be confirmed with Pine Grove or another Rochester dealer; no current posted base price for the R31-26 was found.


Topo and siting

A full topographic review of all three parcels, using USGS 3DEP 1-meter lidar, shaped the cottage placement. The maps below show 2-foot contours, slope, bare-earth viewsheds toward Elk Lake from ground height and from a second-floor or deck height, and line-of-sight profiles between the main house and each candidate pad. They also mark the approximate electric-line corridor (digitized from aerials, not a surveyed easement), existing drives and buildings, driveway grades, and septic-suitable ground (gentle slope, off the corridor, away from the well). These maps are also on the Topo & siting page. They are not a survey. Confirm the recorded easement width with title or the utility, and confirm well, septic, and the real lake view on the ground, preferably leaf-off.

Recommended pad: F, northeast of the front (north) barn on the east land, about 792 ft elevation (17 ft below the house), mean slope about 10%, about 450 ft from the power line. A 190-foot driveway spur can stay around 5% grade. Bare-earth rays toward Elk Lake are mostly clear at both 6 ft and 16 ft eye height; trees will screen or frame the real view. Pad N, further north, is the easiest alternate (flatter, shorter drive) but sits 39 ft below the house and more directly in the north lake-view cone. Pads H and S, east and south of the house, are closer and more exposed, and S is tight to the corridor. Pad A, in the corridor, is not used.

Candidate ranking

10746 E Deal Rd · cottage re-siting after the electric-line corridor · not a survey

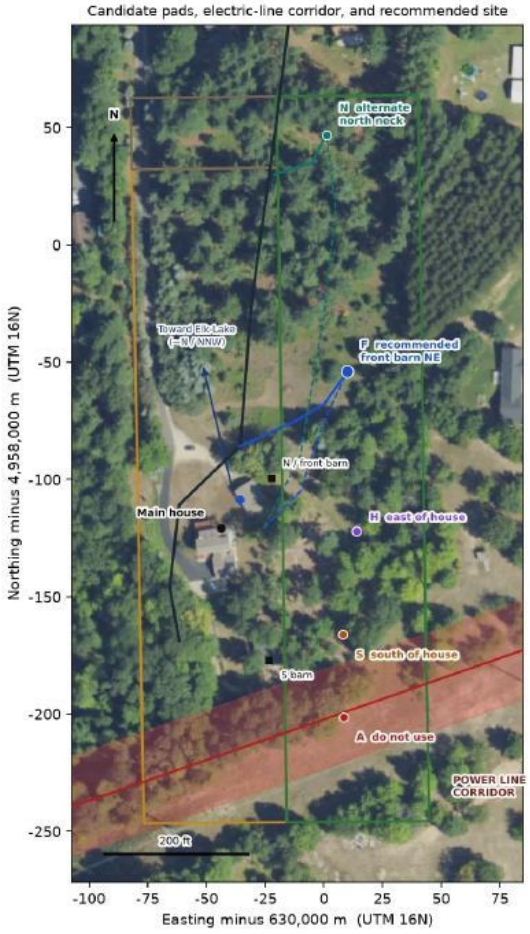

Cottage siting · candidate ranking

10746 E Deal Rd · three parcels · USGS 3DEP 1 m lidar
NOT A SURVEY · confirm the recorded easement width with title / the utility

Recommended: F — northeast of the front (north) barn

The previous cottage pad sat in the open field southeast of the south barn. That field is the cleared electric-line corridor (pads A–D sit in or on it). The cottage has to move.

F is the best match for a site northeast, toward the lake, in the clear space by the front barn. It is on the east land, about 450 ft from the power line, 280 ft from the house, and about 17 ft lower than the house as the ground falls toward the lake. Mean pad slope is about 10%. A short spur of about 190 ft can leave the existing drive north of the house and stay around 5% grade, under the 10% target. Only modest clearing is needed. The north barn and existing trees can help screen it from parts of the house; bare-earth line-of-sight from the decks is still open, so keep and add screening.

N, the north neck, is the easiest pad on paper: about 4% slope, a 100-ft spur, 770 ft from the line, and a strong bare-earth lake view. It sits 39 ft below the house and more directly in the north lake-view cone, and it needs more tree clearing. Use N if an easy pad matters more than screening.

Behind the house: H (due east of the house) is workable but closer and more exposed to the east deck; a drive must skirt the well. S (south of the house) is only about 100 ft from the power line and is tight. Neither is the lead recommendation.

Orientation at F: long axis east-west, porch and main windows facing north / north-northwest toward Elk Lake, south windows for sun. Own driveway off the existing drive; walking trail from the east deck, off the drive. Room for a well and septic on the east land (perc test required). Confirm the recorded easement width, the well and septic locations, and the view on the ground, preferably leaf-off.


F at a glance

F elev: 792 ft	vs house: −17 ft	slope: 9.9% mean
to power line: 450 ft	drive: −190 ft, −5%	lake view*: 88% rays

*Bare-earth viewshed toward Elk Lake; trees can block or frame the real view.


Candidate pads, the approximate electric-line corridor, and the recommended site. Not a survey.

2-foot contours

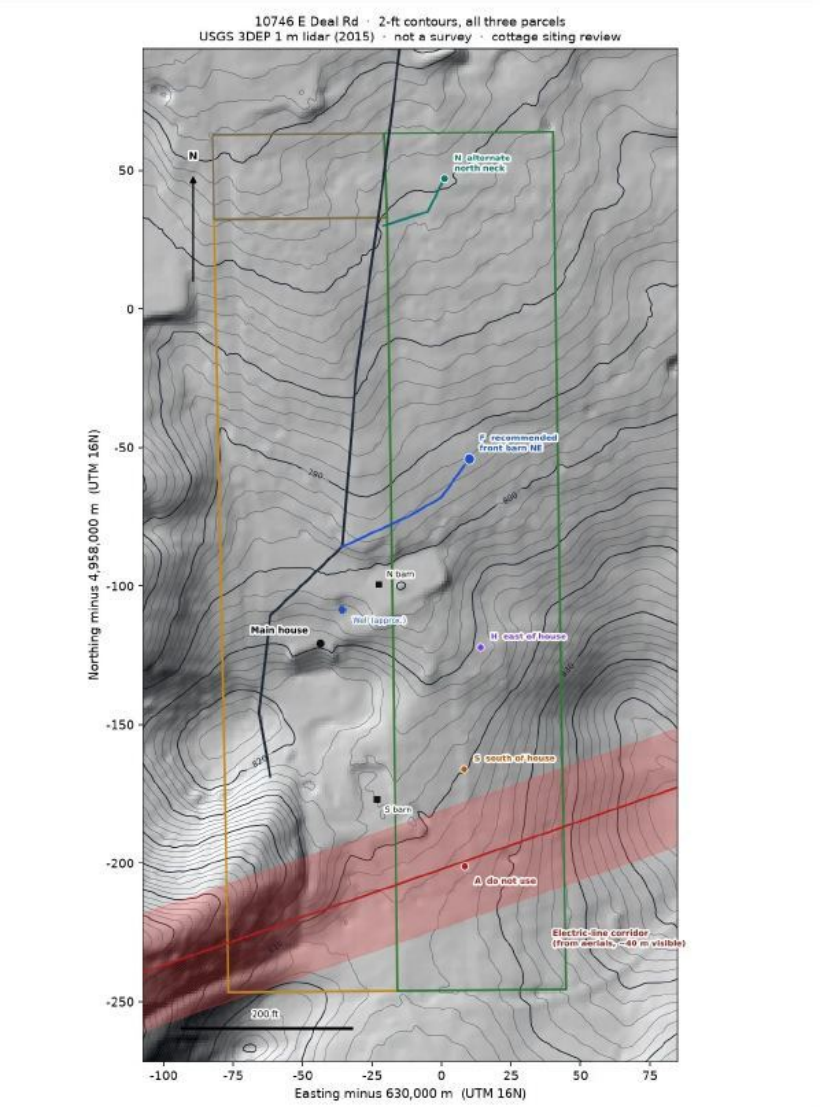


2-ft contours from USGS 3DEP 1 m lidar (2015). Hillshade underlay. Not a survey.

Slope

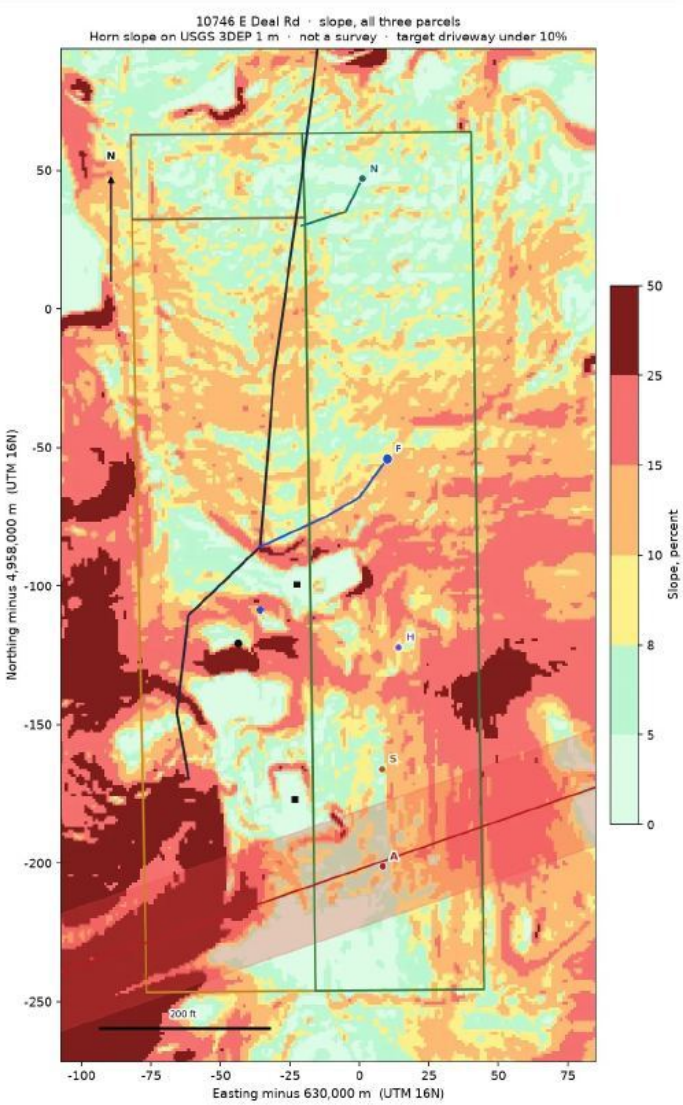


Horn slope on the 1 m DEM. Green is gentler ground, better for a pad, driveway, and septic. Target driveway grade is under 10%. Not a survey.

Viewsheds toward Elk Lake

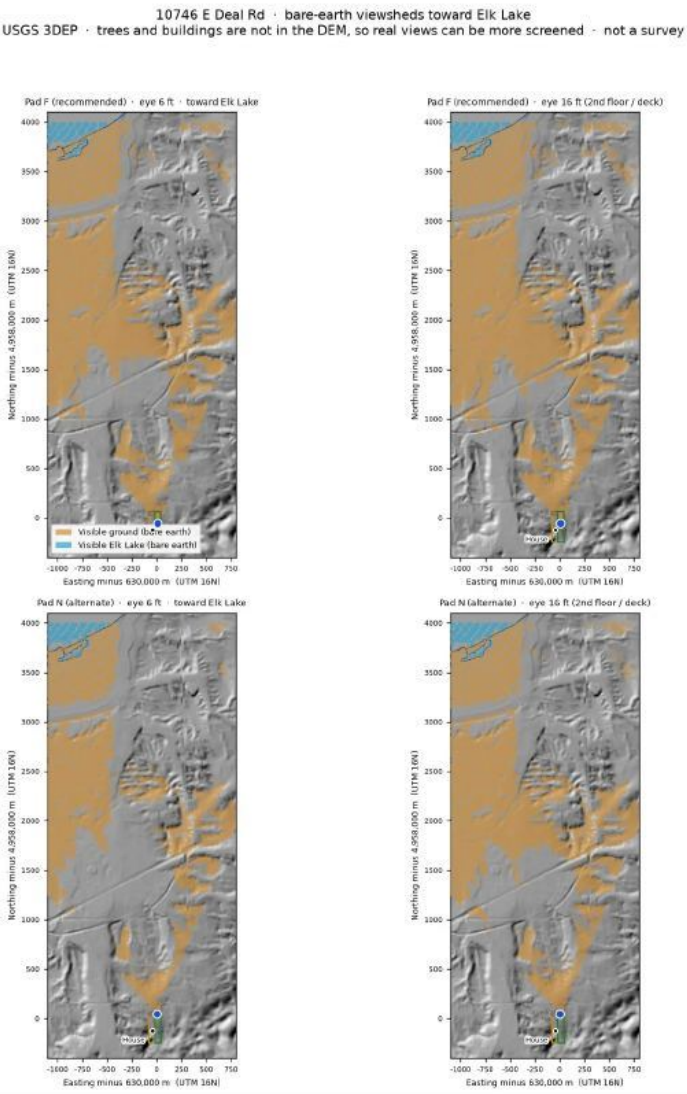

Bare-earth viewsheds from recommended pad F and alternate pad N, at 6 ft and at 16 ft (second floor or deck). Trees and buildings are not in the DEM, so the real view can be more screened. Not a survey.

Elevation profiles and line-of-sight

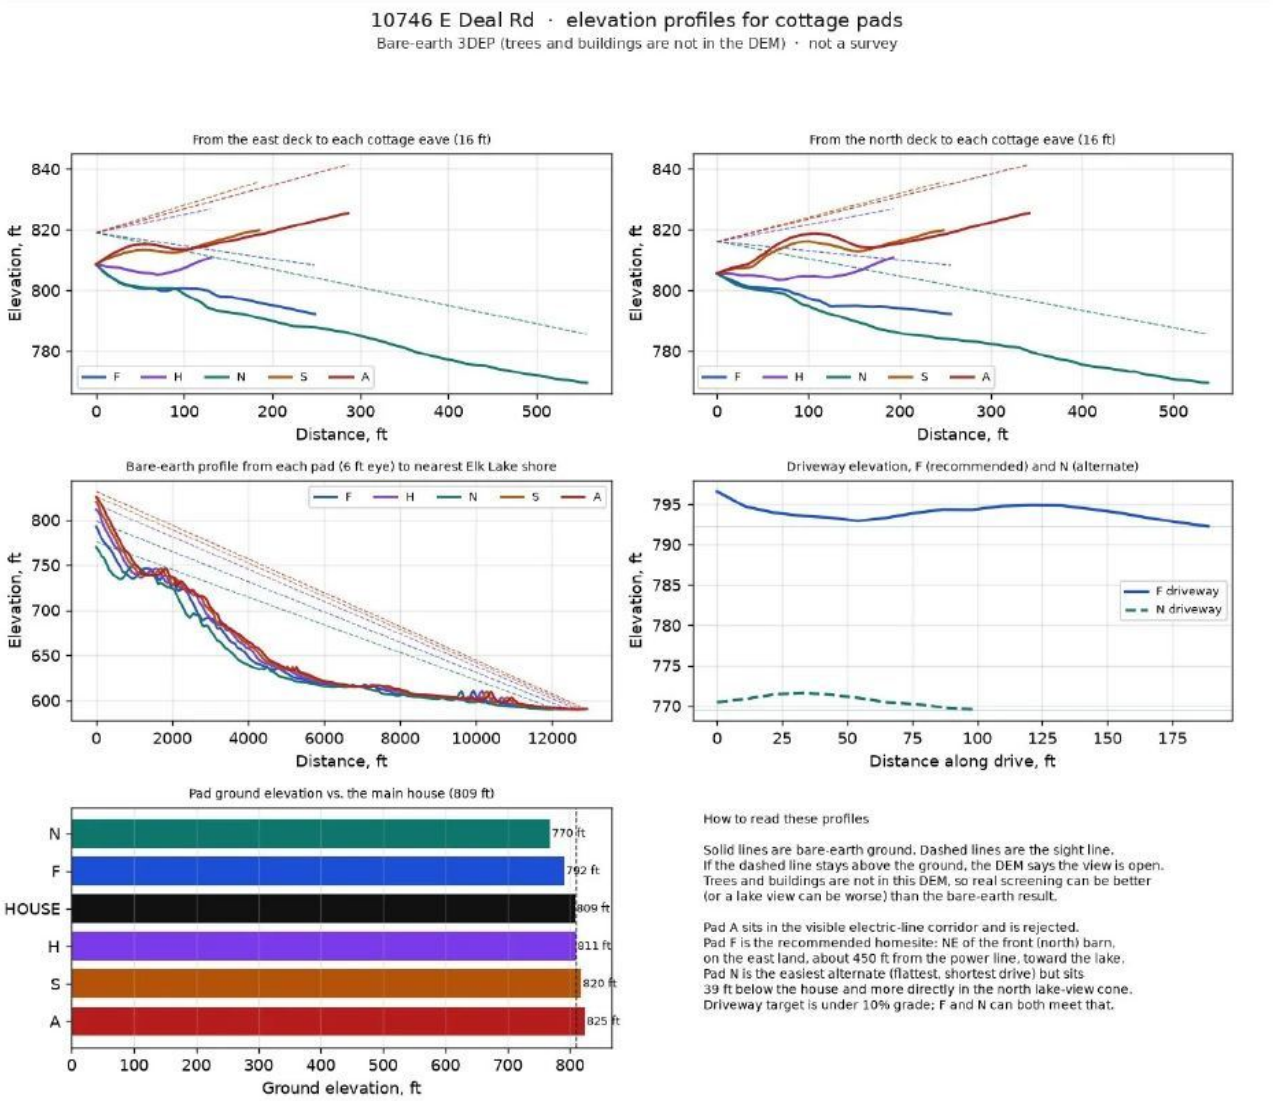

Line-of-sight from the east and north decks to each cottage eave, lake-bound profiles from each pad, and driveway grades for F and N. Dashed lines are sight lines; if they stay above the ground, the bare-earth DEM says the view is open. Not a survey.

Approximate professional costs

These are rough estimates for professional work in Northern Michigan in 2026, not bids. Actual quotes will vary with prep, access, the amount of existing woodwork, and the contractor. Get at least two local bids before budgeting.

Interior painting

Based on about 3,120 finished square feet, 6 bedrooms, and 3.1 baths. The main living room is excluded, because it is kept as-is. On the lower walkout, only the painted drywall is in the wall scope; existing wood paneling, doors, trim, and railings downstairs stay natural and are not painted. Wood ceilings and beams are excluded throughout. Already-white drywall, popcorn, and drop ceilings are also excluded from the base scope.

SCOPE	WHAT'S INCLUDED	LOW	HIGH
Interior walls	Main and upper walls in Shoji White, and lower-walkout drywall in Accessible Beige. The main living room is not included.	$5,000	$10,000

SCOPE	WHAT'S INCLUDED	LOW	HIGH
Trim, doors, railings, and wall paneling	Baseboards, casings, interior doors, closet doors, stair and loft railings, and wood wall paneling on the main and upper levels, in semi-gloss Alabaster — except the living room, which is not painted. Lower-level wood paneling, doors, trim, and railings stay natural and are not included. Wood ceilings and beams are not included.	$7,500	$16,000
Cabinets and vanities	Main kitchen cabinets and island, laundry cabinets, primary vanity and linen cabinet, powder vanity, and the lower-kitchen cabinet, in satin urethane enamel Edgecomb Gray. Assumes degreasing, sanding, and a stain-blocking primer on the existing oak.	$5,500	$12,000
Optional: drywall ceiling refresh	Repaint already-white popcorn, smooth, or drop ceilings where needed. Not required for the look in the photos.	$2,000	$5,000
Interior painting total	**Walls, trim/paneling, and cabinets as scoped above. Optional ceiling refresh not included in this total.**	**$18,000**	**$38,000**

Exterior paint and barns

The existing 2019 roof is kept. No shingle or metal roof replacement is included.

SCOPE	WHAT'S INCLUDED	LOW	HIGH
House exterior painting	Vinyl siding in Alabaster (vinyl-safe product), trim, fascia, soffit, gutters, the walkout door, and deck railings and posts, on a 3,120 sf 2-story house with a walkout and wraparound deck. Deck floor boards are not included.	$12,000	$28,000
Two pole barns plus the yard shed	Repaint or re-coat metal siding, trim, and doors in the matching light-body, black-trim scheme, including the smaller shed in the rear yard.	$6,000	$16,000
Paint only (keep existing roof)	**House and outbuilding painting, no roof work.**	**$18,000**	**$44,000**

Assumptions: professional labor and materials in Northern Michigan in 2026; vinyl siding painted with a vinyl-safe product; stained oak cabinets need a stain-blocking primer; the upper loft will likely need scaffolding or lifts for high trim and railings; metal barn coatings may be a specialized product, not standard house paint. The 2019 house roof is kept in this concept. Cottage build-out costs are in the cottage section, not in these painting totals. These ranges are rough visualizations, not bids.

Download the paint-concept PDF
